

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Name: Rachel Sara Mathew SRN: PES2UG24CS390 Sec: G


1. Jira Backlog with Epics and User Stories

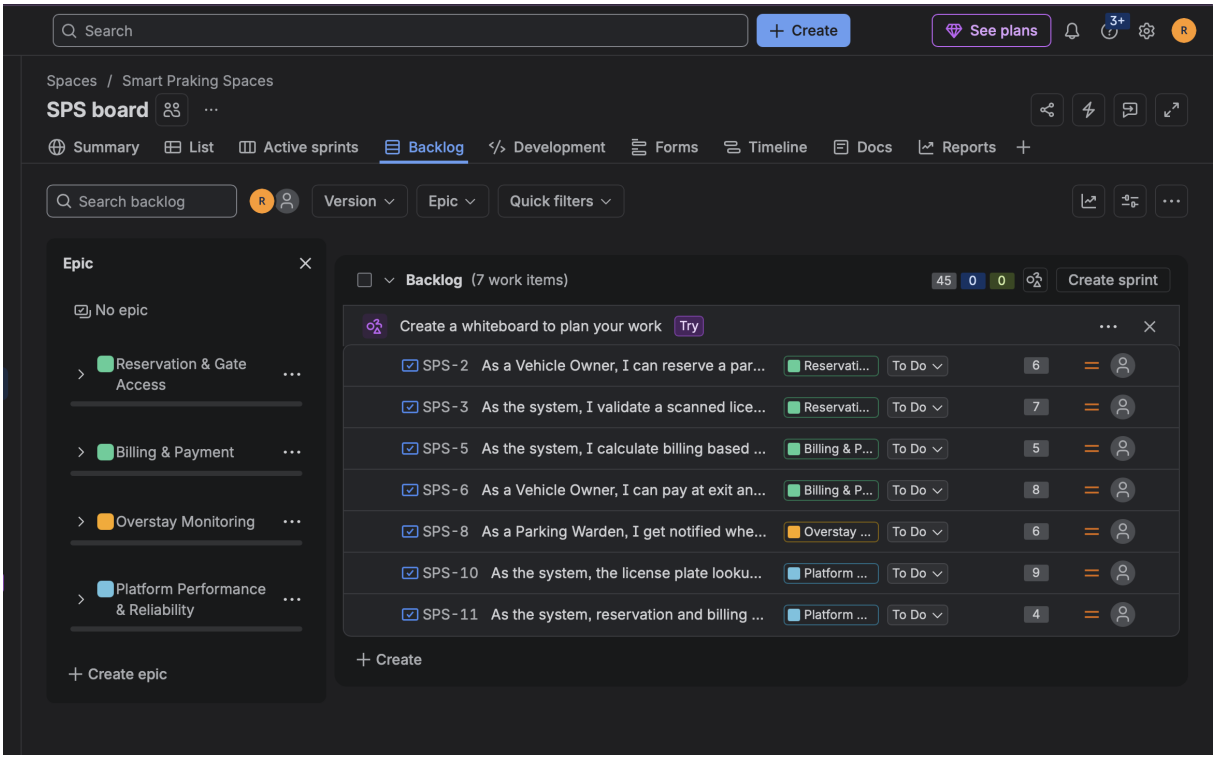

2. Story Point Assignments

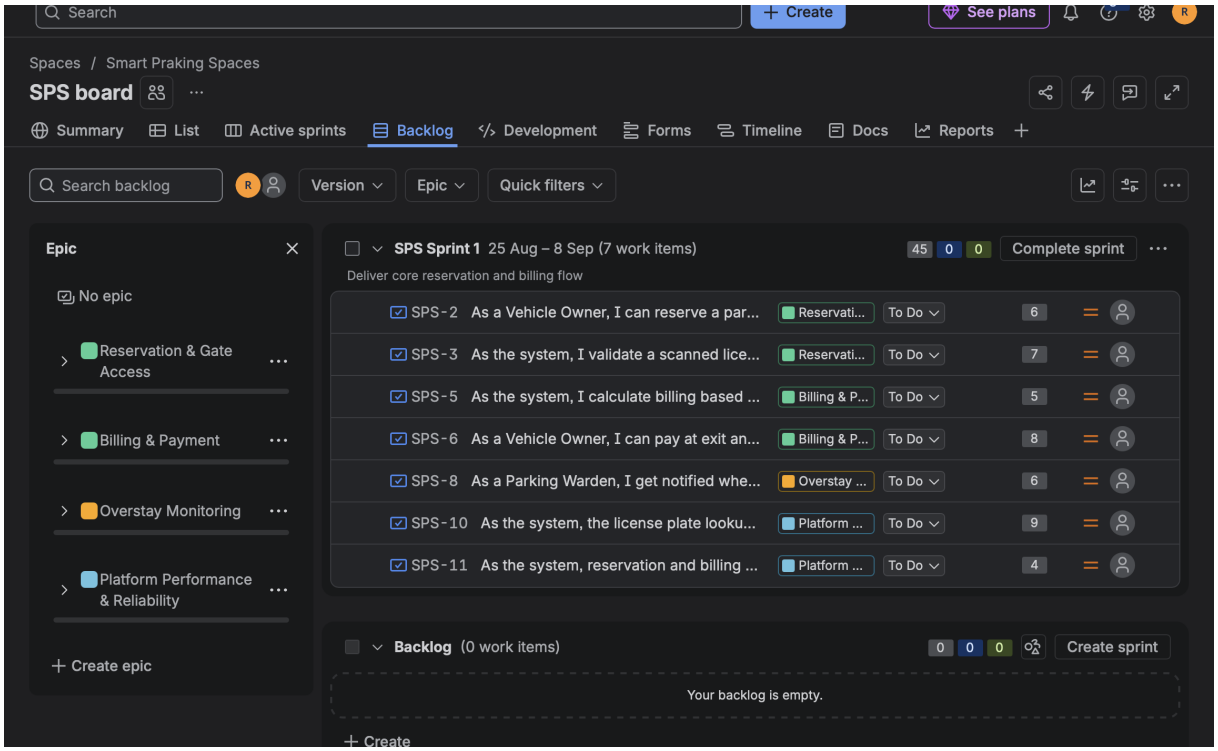

3. Sprint Board (Active Sprint View)

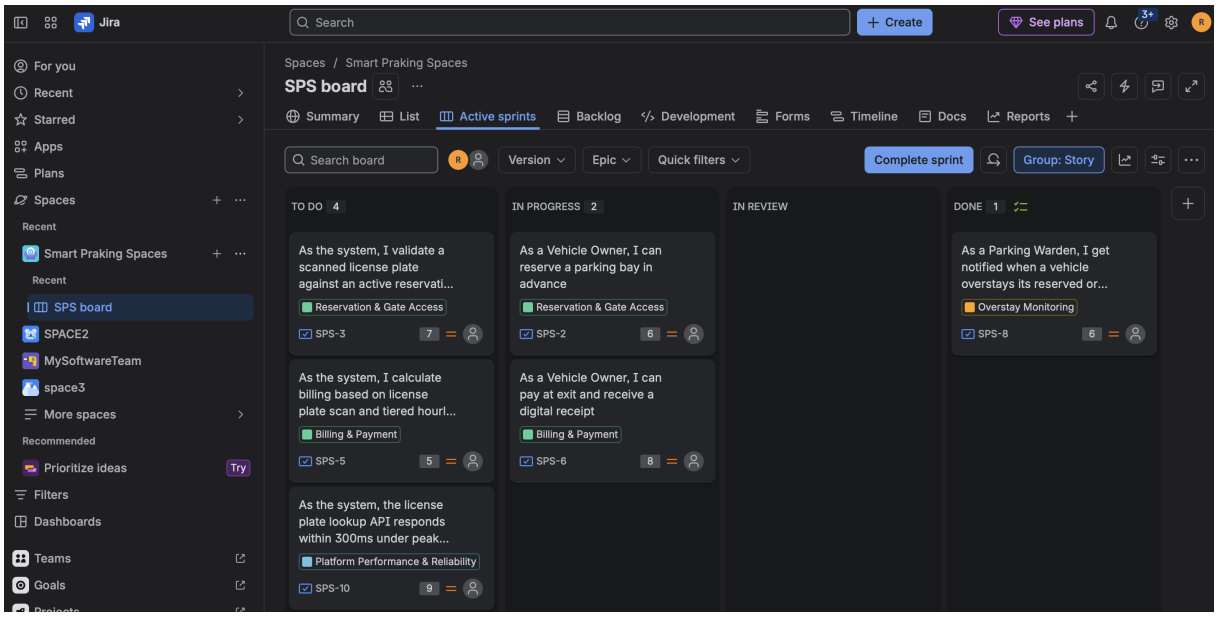

4. Burndown Chart



Date	Issue	Event Type	Event Detail	Story Points Inc.	Story Points Dec.	Story Points Remaining
25/Aug/26 5:52 PM	Total	Sprint start				0
	SPS-2	Scope change	Issue added to sprint	6		6
	SPS-8	Scope change	Issue added to sprint	6		12
	SPS-6	Scope change	Issue added to sprint	8		20
	SPS-5	Scope change	Issue added to sprint	5		25
	SPS-10	Scope change	Issue added to sprint	9		34
	SPS-3	Scope change	Issue added to sprint	7		41
	SPS-11	Scope change	Issue added to sprint	4		45
25/Aug/26 5:55 PM	SPS-8	Burndown	Issue completed		6	39

5. Reflection Questions

1. Did your estimations reflect the actual effort?

Since story points were assigned somewhat arbitrarily rather than through team discussion, they are a rough approximation rather than a precisely calibrated estimate. In a real team setting, running Planning Poker with multiple people would surface disagreements (for example, whether validating a license plate is really more complex than calculating billing) and would produce more consistent, defensible numbers grounded in group consensus.

2. Was your backlog well-prioritized?

The backlog was organized by grouping related functional and non-functional requirements into four epics: Reservation & Gate Access, Billing & Payment, Overstay Monitoring, and Platform Performance & Reliability. This grouping reflects a logical structure by feature area. However, priority levels (High, Medium, Low) were not explicitly differentiated beyond the default Medium setting. A more rigorous prioritization pass would rank core revenue and safety-critical features, such as billing and gate access, more visibly above secondary features like overstay notifications.

3. How did your simulated sprint align with your plan?

All 7 stories, totaling 45 story points, were pulled into Sprint 1 rather than a scoped-down subset, which is heavier than what a realistic one-week sprint would typically carry. During the simulation, only 1 of the 7 stories was moved to Done, while others progressed to In Progress or remained in To Do. This shows that in a real sprint, this scope would likely be too large to complete within the timebox, illustrating the importance of avoiding overcommitment during sprint planning.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed a modest drop from 45 to 39 remaining story points, reflecting the single completed story, while still sitting well above the ideal guideline line. This suggests that if this pace continued, the sprint would finish with significant work remaining. It serves as an early warning sign that either the sprint scope was too large for the timebox, or that velocity assumptions need to be recalibrated for future sprints based on actual completion rates rather than initial estimates.
